

Weekly Construction Summary

Week of 10/22/2023

Construction Summary

Loading of the BUS sections into shipping containers began, as the first two “sleds” and containers were delivered to the site at the end of last week after two weeks of there being no outside activity at the site.

On Monday, one of the two large central sections and two of the four small sections were loaded into a container, and work on securing the sections in the container commenced.

On Tuesday, the second of the two large central sections and the last two of the four small sections were loaded into a container. Work continued on securing the BUS sections in the containers for shipment.

Loading the remaining two large BUS sections is pending the arrival of the second pair of “sleds” and containers.



INDEPENDENT DECOMMISSIONING PROJECT MANAGER PROJECT DIARY

DATE : Monday, October 23, 2023

PROJECT TITLE: **Caltech Submillimeter Observatory Decommissioning**

Report By: **Shawn Gardner**

WEATHER: Suitable For All Planned Work

At CSO, partly cloudy, light-moderate wind. Temp at 8:00am 45F.

Increasing wind and cloudiness in the afternoon.

Work Hours:

Arrv: **0800**

Dep: **1500**

Monitors on Site:	Cultural - Peter Alu Construction - Karl Halemano
Work Items	Location & Description of Work/Activities
Telescope removal	Packing BUS sections in shipping containers. One of the two large central sections and two of the four small sections were loaded into a container. Note: the two containers previously onsite have been removed, and two 40-foot containers and BUS sleds were delivered to the site last week.
Demolition	No additional demo work planned until Spring 2024. Removal of transformer by HELCO and comms disconnection by Hawaiian Telcom expected to be conducted in November 2023 or as scheduling allows.

WORK FORCE & EQUIPMENT

NAME	POS	HR	Company	EQUIPMENT	MODEL/TYPE	HR
Bill Johnson		0		Container x2	40 ft	Onsite
Rick	Crew	8		Telehandler, JLG Skytrak	10054	7
George	Crew	8				
Sayer	Crew	8				
Sam Peck	Sup.	0	GBI			
Keoni Kaluna	Foreman	0	GBI			
Frank Collo	Operator	0	GBI			
Bruce Burley	Foreman	0	Northwest Demo.			
Darren Miguel	Crew	0	Northwest Demo.			
Anthony Ortiz	Crew	0	Northwest Demo.			
Gary Lagapa	Crew	0	Northwest Demo.			

Signed by: 

Reviewed by: Shawn Gardner

Date 10/23/2023



^ 10:49am - lifting large BUS section



^ 11:43am - large BUS section secured to sled




^ 11:57am - inserting sled with BUS section in container



^ 12:50pm - lifting first small section



^ 12:51pm - putting first small section in container

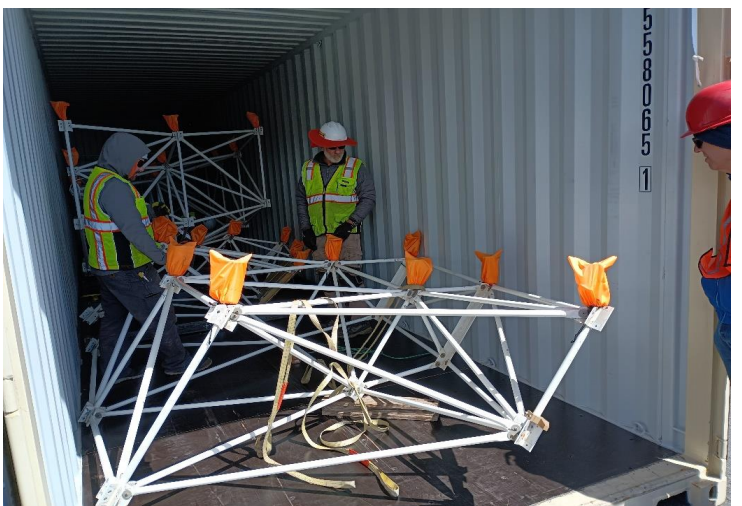

^ 1:05pm - three sections in container



INDEPENDENT DECOMMISSIONING PROJECT MANAGER PROJECT DIARY

DATE : Tuesday, October 24, 2023

WEATHER: Suitable For All Planned Work
At CSO, clear, moderate wind. Temp at
8:00am 45F.

PROJECT TITLE: **Caltech Submillimeter Observatory Decommissioning**

Work Hours:

Report By: **Shawn Gardner**

Arrv: **0800**

Dep: **1430**

Monitors on Site:	Cultural - Peter Alu
Work Items	Location & Description of Work/Activities
Telescope removal	Packing BUS sections in shipping containers. The second of the two large central sections and the last two of the four small sections were loaded into a container.
Demolition	No additional demo work planned until Spring 2024. Removal of transformer by HELCO and comms disconnection by Hawaiian Telcom expected to be conducted in November 2023 or as scheduling allows.

WORK FORCE & EQUIPMENT

NAME	POS	HR	Company	EQUIPMENT	MODEL/TYPE	HR
Bill Johnson		0		Container x2	40 ft	Onsite
Rick	Crew	8		Telehandler, JLG Skytrak	10054	7
George	Crew	8				
Sayer	Crew	8				
Sam Peck	Sup.	0	GBI			
Keoni Kaluna	Foreman	0	GBI			
Frank Collo	Operator	0	GBI			
Bruce Burley	Foreman	0	Northwest Demo.			
Darren Miguel	Crew	0	Northwest Demo.			
Anthony Ortiz	Crew	0	Northwest Demo.			
Gary Lagapa	Crew	0	Northwest Demo.			

Signed by: 

Reviewed by: Shawn Gardner

Date 10/24/2023



^ 8:44am - prepping sled and BUS section



^ 9:09am - lifting BUS section



^ 10:41am - BUS section secured to sled



^ 11:03am - inserting sled and BUS section into container



^ 11:39am - three sections in container



^ 2:16pm - done for the day
