



INDEPENDENT DECOMMISSIONING PROJECT MANAGER (IDPM) WEEKLY REPORT

WEEK ENDING: Friday, September 16, 2022

PROJECT TITLE: CALTECH SUBMILLIMETER OBSERVATORY DECOMMISSIONING

BY: Pedro Foronda

WEATHER : Good For All Planned Work

- | | |
|--|---|
| <input checked="" type="checkbox"/> Clear-pm | <input type="checkbox"/> Light Showers am |
| <input type="checkbox"/> Partly Cloudy | <input type="checkbox"/> Passing Rains-am |
| <input type="checkbox"/> Cloudy-pm | <input type="checkbox"/> Rain - am |
| <input type="checkbox"/> Overcast | <input type="checkbox"/> Windy |

Work Items	
Perimeter Fence	<p>Work Observed: 9/13/22 (Tues) 0700 Hrs. <i>Island Wide Fencing, Inc.</i> crew arrived on site in a flat bed truck loaded with fence materials.</p> <p>Prior to the start of work: Safety Briefing: I reminded the crew of the need to be aware of altitude sickness symptoms such as headache and shortness of breath at rest. Bill Johnson shared that there are Oxygen bottles, Oxygen saturation meter and first aid kit available inside the telescope observatory.</p> <p>Ronald Mitchell, the Cultural Monitor guided the group in a small "Pule or prayer".</p> <p>The Invasive Species Inspection Certificate was verified to be current and approved by J. Miyashiro.</p> <p>The wire perimeter fence was installed in accordance with the included plan and detail below. The fence work was completed at 1300 Hrs. and Island Wide Fencing did not have to return the following day, Wednesday, as was originally anticipated.</p> <p>Directions Given: IDPM - Directed to increase the depth of driveway posts to the minimum 18in depth before pouring concrete. Cultural Monitor - None Archaeological Monitor - None</p> <p>Misc. Notes: Wallace Ishibashi of UH visited the site to check on the progress. Bill Johnson was working inside the observatory.</p>

WORK FORCE & EQUIPMENT

NAME	POS	HR		NAME	POS	HR	EQUIPMENT	TYPE	HR
Steven Matsuura	Foreman	8	Island wide fencing				Flat Bed Crew Truck	Ford 150	8
Gerry Kansou	Labor	8	Island wide fencing						
Orion Inosensio	Labor	8	Island wide fencing						
Ronald Mitchell	Cultural Monitor	8	Kulaiwi Archaeology						
Robynn Luiz	Archaeological Monitor	8	ASM Affiliates						

Signed by:

Pedro Foronda, P.E.

Reviewed by:

William Wanner, P.E., CCM

Date

9/16/2022



INDEPENDENT DECOMMISSIONING PROJECT MANAGER (IDPM) WEEKLY REPORT

WEEK ENDING: Friday, September 16, 2022


PROJECT TITLE: CALTECH SUBMILLIMETER OBSERVATORY DECOMMISSIONING

BY: Pedro Foronda

WEATHER : Good For All Planned Work

- ☒ Clear-pm ☐ Light Showers am
☐ Partly Cloudy ☐ Passing Rains-am
☐ Cloudy-pm ☐ Rain - am
☐ Overcast ☐ Windy

PHOTOS *(full resolution photos archived)*

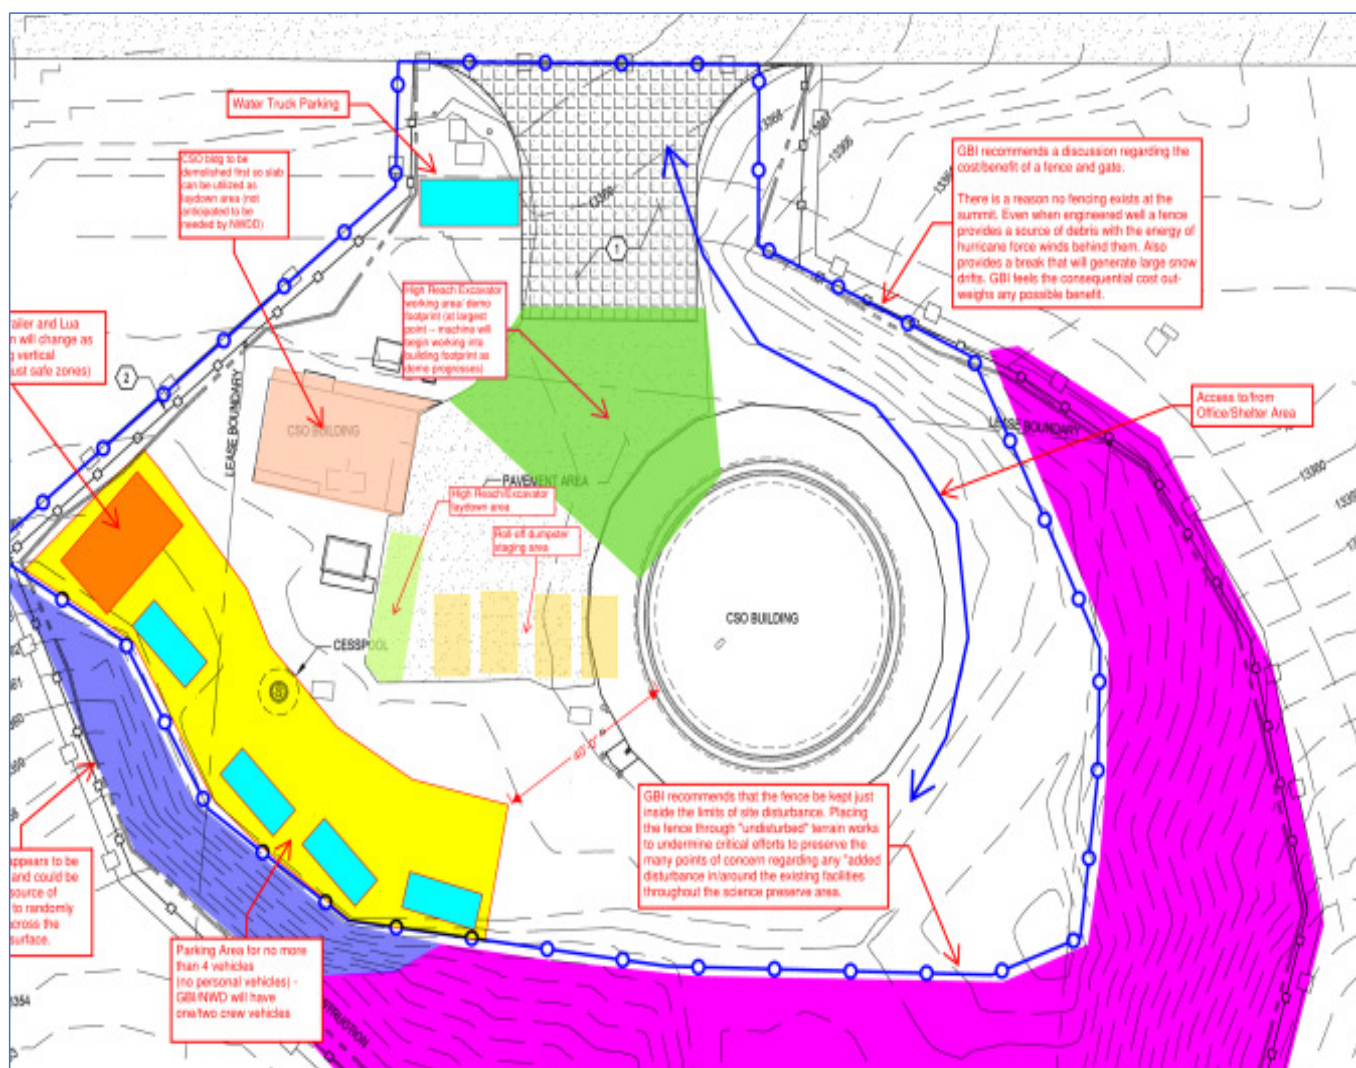

Worksite Perimeter Fence Plan



INDEPENDENT DECOMMISSIONING PROJECT MANAGER (IDPM) WEEKLY REPORT


WEEK ENDING: Friday, September 16, 2022

PROJECT TITLE: CALTECH SUBMILLIMETER OBSERVATORY DECOMMISSIONING

BY: Pedro Foronda

WEATHER : Good For All Planned Work

<input checked="" type="checkbox"/> Clear-pm	<input type="checkbox"/> Light Showers am
<input type="checkbox"/> Partly Cloudy	<input type="checkbox"/> Passing Rains-am
<input type="checkbox"/> Cloudy-pm	<input type="checkbox"/> Rain - am
<input type="checkbox"/> Overcast	<input type="checkbox"/> Windy

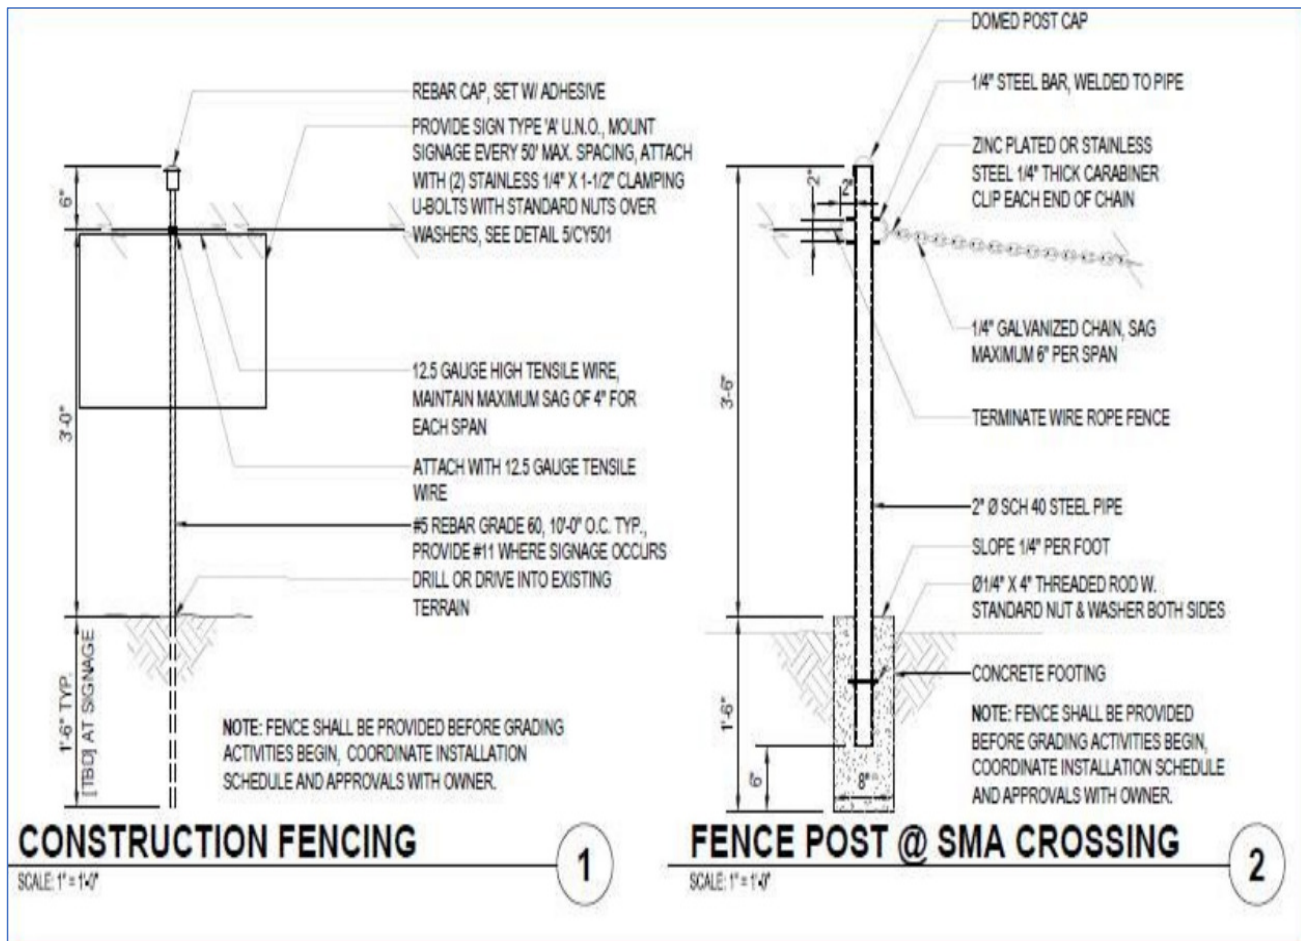

Fence Detail



INDEPENDENT DECOMMISSIONING PROJECT MANAGER (IDPM) WEEKLY REPORT

WEEK ENDING: Friday, September 16, 2022

PROJECT TITLE: CALTECH SUBMILLIMETER OBSERVATORY DECOMMISSIONING

BY: Pedro Foronda

WEATHER : Good For All Planned Work

- | | |
|--|---|
| <input checked="" type="checkbox"/> Clear-pm | <input type="checkbox"/> Light Showers am |
| <input type="checkbox"/> Partly Cloudy | <input type="checkbox"/> Passing Rains-am |
| <input type="checkbox"/> Cloudy-pm | <input type="checkbox"/> Rain - am |
| <input type="checkbox"/> Overcast | <input type="checkbox"/> Windy |



Fence Post Installation



INDEPENDENT DECOMMISSIONING PROJECT MANAGER (IDPM) WEEKLY REPORT


WEEK ENDING: Friday, September 16, 2022

PROJECT TITLE: CALTECH SUBMILLIMETER OBSERVATORY DECOMMISSIONING

BY: Pedro Foronda

WEATHER : Good For All Planned Work

- | | |
|--|---|
| <input checked="" type="checkbox"/> Clear-pm | <input type="checkbox"/> Light Showers am |
| <input type="checkbox"/> Partly Cloudy | <input type="checkbox"/> Passing Rains-am |
| <input type="checkbox"/> Cloudy-pm | <input type="checkbox"/> Rain - am |
| <input type="checkbox"/> Overcast | <input type="checkbox"/> Windy |

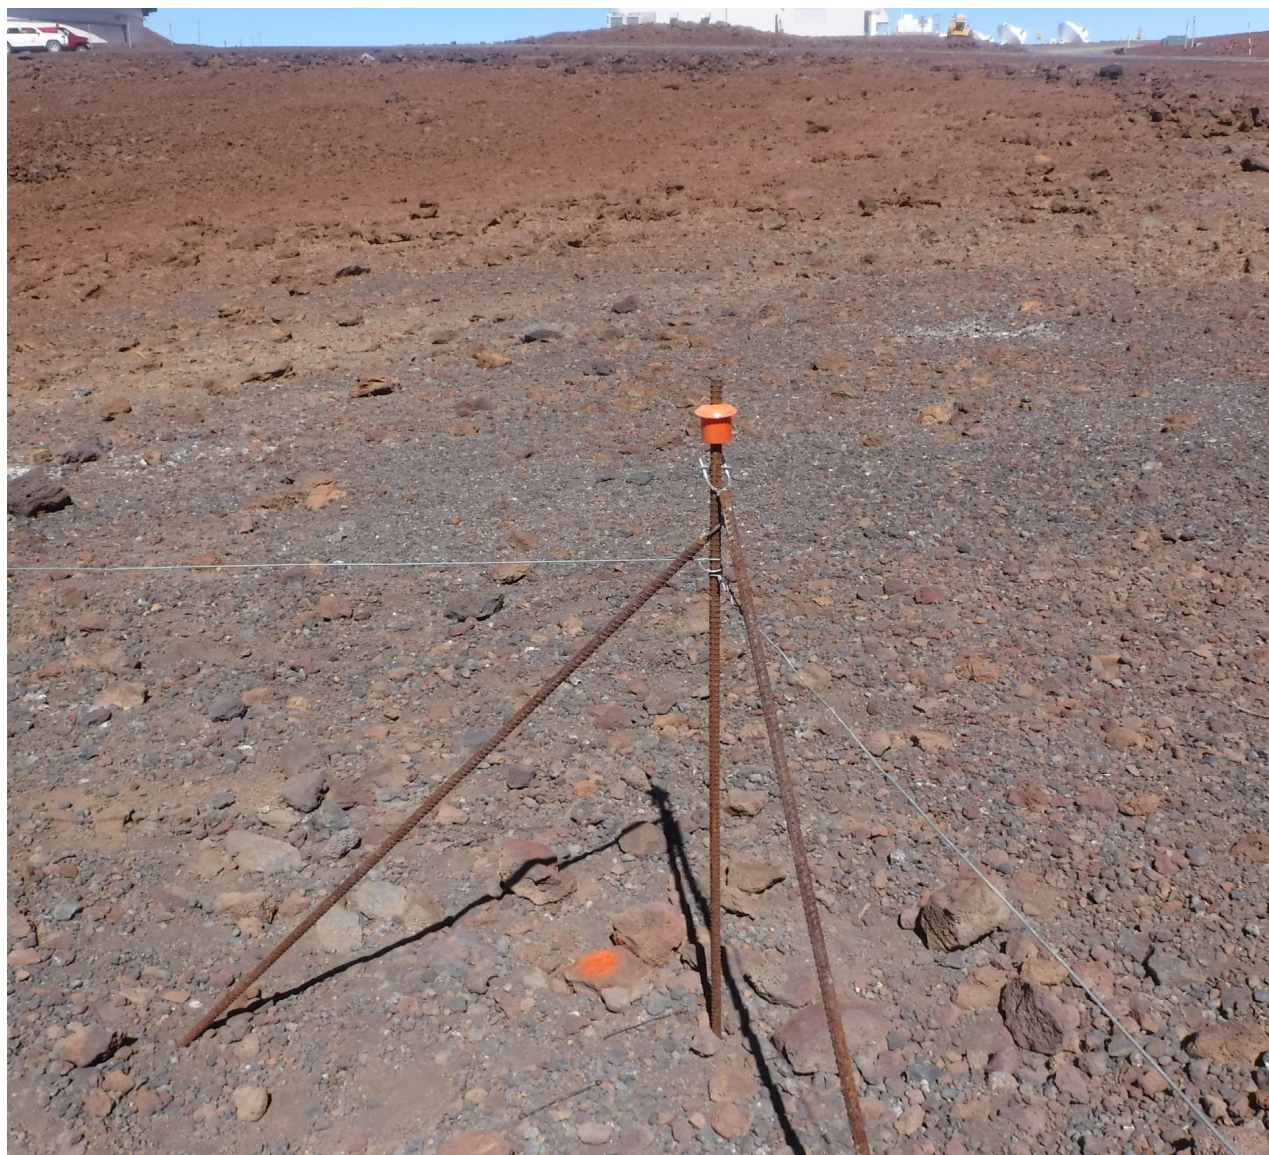

No. 5 Rebar Wire Fence



INDEPENDENT DECOMMISSIONING PROJECT MANAGER (IDPM) WEEKLY REPORT


WEEK ENDING: Friday, September 16, 2022

PROJECT TITLE: CALTECH SUBMILLIMETER OBSERVATORY DECOMMISSIONING

BY: Pedro Foronda

WEATHER : Good For All Planned Work

- | | |
|--|---|
| <input checked="" type="checkbox"/> Clear-pm | <input type="checkbox"/> Light Showers am |
| <input type="checkbox"/> Partly Cloudy | <input type="checkbox"/> Passing Rains-am |
| <input type="checkbox"/> Cloudy-pm | <input type="checkbox"/> Rain - am |
| <input type="checkbox"/> Overcast | <input type="checkbox"/> Windy |

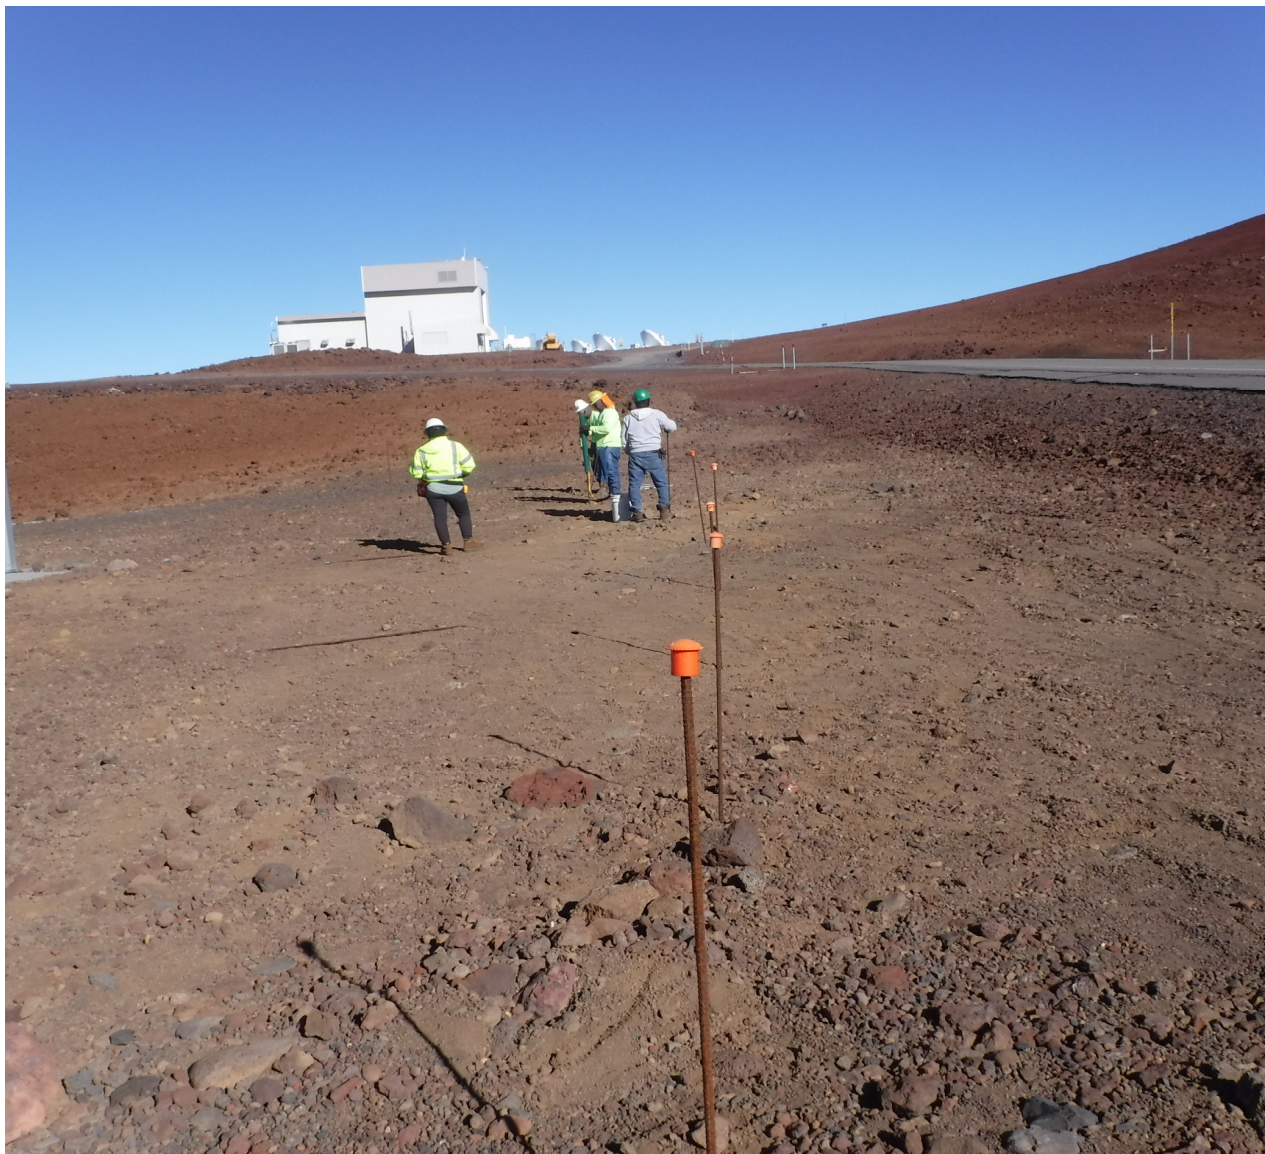

Fence Installation Crew



INDEPENDENT DECOMMISSIONING PROJECT MANAGER (IDPM) WEEKLY REPORT


WEEK ENDING: Friday, September 16, 2022

PROJECT TITLE: CALTECH SUBMILLIMETER OBSERVATORY DECOMMISSIONING

BY: Pedro Foronda

WEATHER : Good For All Planned Work

- | | |
|--|---|
| <input checked="" type="checkbox"/> Clear-pm | <input type="checkbox"/> Light Showers am |
| <input type="checkbox"/> Partly Cloudy | <input type="checkbox"/> Passing Rains-am |
| <input type="checkbox"/> Cloudy-pm | <input type="checkbox"/> Rain - am |
| <input type="checkbox"/> Overcast | <input type="checkbox"/> Windy |

 **INVASIVE SPECIES INSPECTION CERTIFICATE** No. 01100

APPROVED

Date and Time: 9/16/22 8:20 am
Expiration date and time: 9/16/22 8:30 am
Destination: Cal-Tech
Vehicle Lic/Descrip: _____
Cargo Description: Rebar, tools, generator
Toll used? Yes ☐ No ☒

DELIBERATE NON-COMPLIANCE

REJECTED

Delivery is: _____
Inspector: J. Miyashiro
Inspection location: Island Wide Ferry
Facility/Representative: Steve
Concerns identified: none
Remediation taken: none
Rush inspection? Yes ☐ No ☒

NON-COMPLIANCE (UNAWARE)

This certificate is proof that the inspection is valid for the stated vehicle, cargo, destination, and time frame.
Drivers should keep this certificate in vehicle when making delivery.
For more information please visit: www.malamamaunakea.org/inspections/

Invasive Species Inspection Certificate
