

Weekly Construction Summary

Week of 05/05/2024

Construction Summary

No demolition work this week due to forecasted high winds.

On Monday, the shutter cylinders were removed from the site, and the site was prepared for the expected winds.

Daily report attached.



INDEPENDENT DECOMMISSIONING PROJECT MANAGER PROJECT DIARY

DATE : Monday, May 6, 2024

WEATHER: Wind too high for Planned Work
At CSO, partly cloudy, very windy. Temp
at 10am 35F. Up to high 30s at noon.

PROJECT TITLE: **Caltech Submillimeter Observatory Decommissioning**

Work Hours:

Report By: **Shawn Gardner**

Arrv: **0945**

Dep: **1200**

Monitors on Site:	Cultural - Peter Alu
Work Items	Location & Description of Work/Activities
Demolition	<p>Morning meeting was at 0830 due to crews flying in from Oahu. Summit weather showed winds too high for demolition work, and forecast to be about the same all week. Demolition was cancelled, and the situation will be re-evaluated at the Wednesday meeting.</p> <p>Personnel arrived at the CSO between 0930 and 1000. Work began on securing the site for wind. Debris on the first level floor of the structure was shoveled and swept into the pit, and the pit was covered with plastic, which was secured with various pieces of heavy debris, and the excavator bucket.</p> <p>The truck from Conen's arrived to pick up the shutter cylinders at 1000. The cylinders were loaded on the truck and removed from the Mauna without incident.</p> <p>The cleanup/securing was completed and all personnel left the site by 1145.</p>

WORK FORCE & EQUIPMENT

NAME	POS	HR	Company	EQUIPMENT	MODEL/TYPE	HR
Jon Steen		3	GBI	20' Container		
Bronson Sylva		3	GBI	Loader	CAT 950 GC	
Brandon Kepano		3	GBI	Excavator	Volvo EC300DL	
Keala Drummondo		3	GBI	High Reach Excavator	Volvo EC480E HR	
				Sunbelt rental manlift	JLG 660SJ	
Bruce Burley		3	NW Demo			
Anthony Ortiz		3	NW Demo			
Darren Whittaker		3	NW Demo			
Jeff Abella		3	Unitek			
Jone Abella		3	Unitek			
Jomhel Ebuon		3	Unitek			
Calvin Arca		3	Lehua Environmental			


Signed by: 

Reviewed by: Shawn Gardner

Date 5/6/2024



^ 10:35am - shutter cylinders loaded

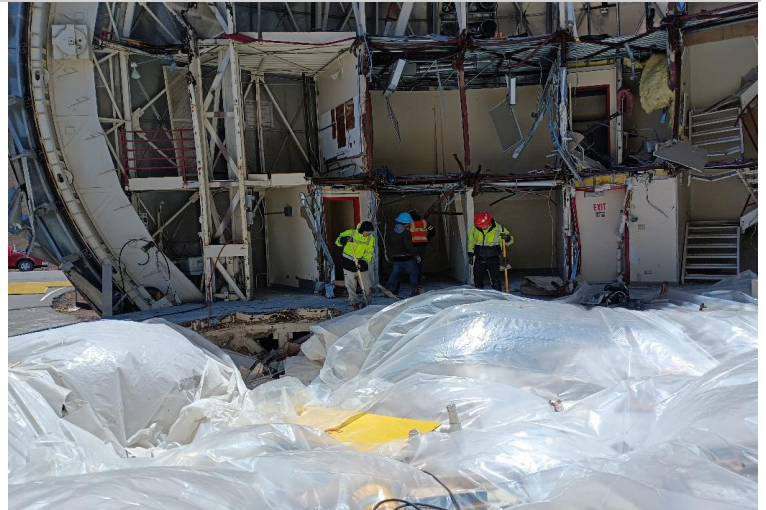

^ 11:08am - cleanup in progress



^ 11:32am - plastic hold down



^ 11:36am - groundsheet hold down



^ 11:38am - drip pan secured



^ 11:46am - site closed for the day



INVASIVE SPECIES INSPECTION CERTIFICATE

No. 00698

APPROVED

Delivery is:

REJECTED

Date and Time: 5/6/24 8:05 am

Expiration date and time: 5/10/24 8:05 am

Destination: CSO

Vehicle Lic/Descrip: 992 HEL

Cargo Description: _____

Bait used? Yes ☒ No

Inspector: J. Miyashiro

Inspection location: Corens

Facility/Representative: _____

Concerns identified: none

Remediation taken: none

Rush inspection? ☒ Yes ☐ No

DELIBERATE NON-COMPLIANCE

NON-COMPLIANCE (UNAWARE)

This certificate is proof that the inspection is valid for the stated vehicle, cargo, destination, and time frame.

Drivers should keep this certificate in vehicle when making delivery.

For more information please visit: www.malamamaunakea.org/inspections/
